



# Board Meeting

April 18, 2023

- **Construction Updates**
  - Elementary Schools (Mina, CCE, COE and CRE)
  - Bastrop High School
  - Cedar Creek High School
- **Design Updates**
  - Intermediate Schools
  - Middle Schools
  - Elementary Schools
  - CRCA
- **Schedule Updates**







# New Elementary- Colony Oaks






## ES1 - Building:

- Area A&B Texture/1<sup>st</sup> Coat Paint – in progress 2nd floor
- Area A&B Ceramic Tile – in progress
- Area A&B Low-Voltage Cabling – in progress
- Area C&D insulation/sheetrock – in progress
- Area C&D Overhead – in progress
- Area C&D Masonry – in progress at Gym/Cafeteria
- Area C & D Storefront Frames – in progress
- Area C&D MEP in-wall rough/OH – in progress
- Roofing – white cap in progress Area B
- Area C&D Tape/Float – in progress
- Area A&B Ceiling Grid 1<sup>st</sup> Floor – in progress
- Area A&B Light Fixtures/Diffusers 1<sup>st</sup> Floor – in progress
- Casework A&B – 4/3
- Exterior Tiltwall Stain – 4/10
- Area C&D Ceramic Tile – 4/17

## Site

- Site Utilities – in progress
- Light pole bases – in progress
- Canopy foundation – in progress
- Flat work – in progress
- Curbs – 4/10

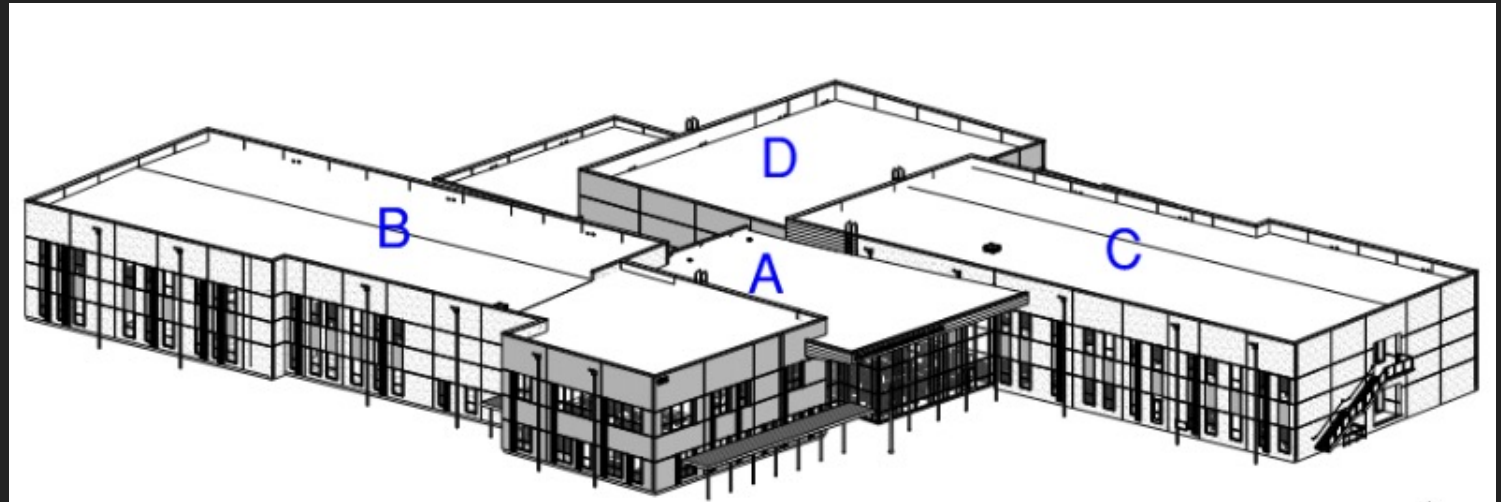









Front Entrance





Reception





Clinic Toilet A105







LGI A202





Library





Stage





Kitchen







Plan SW corner looking at Area C exterior
